

**FIVE PALMS
PRELIMINARY SCHEDULE**

ID	Task Name	Duration	Start	Finish	Predecessors	June					July				
						5/22	5/29	6/5	6/12	6/19	6/26	7/3	7/10	7/17	
1	Procurement	98 days	Wed 6/1/11	Fri 10/14/11											
2	Design	23 days	Wed 6/1/11	Fri 7/1/11											
3	Budgeting	10 days	Mon 7/4/11	Fri 7/15/11 2											
4	Approval	5 days	Mon 7/18/11	Fri 7/22/11 3											
5	Site lighting	60 days	Mon 7/25/11	Fri 10/14/11 4											
6	Coral tiles	40 days	Mon 7/25/11	Fri 9/16/11 4											
7	Roof trusses	30 days	Mon 7/25/11	Fri 9/2/11 4											
8	Roof tiles	30 days	Mon 7/25/11	Fri 9/2/11 4											
9	Exterior doors	25 days	Mon 7/25/11	Fri 8/26/11 4											
10	Finish hardware	20 days	Mon 7/25/11	Fri 8/19/11 4											
11	Hurricane shutters	25 days	Mon 7/25/11	Fri 8/26/11 4											
12	Sun shades	25 days	Mon 7/25/11	Fri 8/26/11 4											
13	A/C Systems	40 days	Mon 7/25/11	Fri 9/16/11 4											
14	Generator	60 days	Mon 7/25/11	Fri 10/14/11 4											
15	Electrical fixtures	60 days	Mon 7/25/11	Fri 10/14/11 4											
16															
17	Sitework	83 days	Mon 7/25/11	Wed 11/16/11											
18	Rough Site	3 days	Mon 7/25/11	Wed 7/27/11 4											
19	Underground utilities	2 days	Thu 7/28/11	Fri 7/29/11 18											
20	Install generator	3 days	Mon 10/17/11	Wed 10/19/11 14											
21	Site lighting	5 days	Thu 11/10/11	Wed 11/16/11 24											
22	Site concrete	10 days	Mon 8/29/11	Fri 9/9/11 29											
23	Stonework	20 days	Mon 9/12/11	Fri 10/7/11 22											
24	Finish grade	3 days	Mon 11/7/11	Wed 11/9/11 37											
25	Landscaping	5 days	Thu 11/10/11	Wed 11/16/11 24											
26															
27	Building	86 days	Mon 8/1/11	Mon 11/28/11											
28	Slab	5 days	Mon 8/1/11	Fri 8/5/11 19											
29	CMU	15 days	Mon 8/8/11	Fri 8/26/11 28											
30	Roof truss system	5 days	Mon 8/29/11	Fri 9/2/11 29											
31	Roof close in	20 days	Wed 8/31/11	Tue 9/27/11 30FS-3 days											
32	Gutter / Downspouts	3 days	Mon 9/26/11	Wed 9/28/11 31FS-2 days											
33	Set exterior doors	3 days	Wed 9/28/11	Fri 9/30/11 31											


Project: Five Palms Prelim 01Jun11 Date: Wed 6/1/11	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

FIVE PALMS
PRELIMINARY SCHEDULE

ID	Task Name	Duration	Start	Finish	Predecessors	June						July		
						5/22	5/29	6/5	6/12	6/19	6/26	7/3	7/10	7/17
34	Exterior stucco	15 days	Mon 10/3/11	Fri 10/21/11 33	34FS-5 days									
35	Exterior painting	10 days	Mon 10/17/11	Fri 10/28/11										
36	Hurricane shutters	3 days	Mon 10/31/11	Wed 11/2/11 35										
37	Sunshade	2 days	Thu 11/3/11	Fri 11/4/11 36										
38	Interior framing	5 days	Wed 9/28/11	Tue 10/4/11 31										
39	Interior plaster	20 days	Wed 10/5/11	Tue 11/1/11 38										
40	Flooring	5 days	Wed 11/2/11	Tue 11/8/11 39										
41	Interior painting	5 days	Wed 11/9/11	Tue 11/15/11 40										
42	A/C Systems	30 days	Wed 9/28/11	Tue 11/8/11 31										
43	Electrical Rough	5 days	Wed 10/5/11	Tue 10/11/11 38										
44	Electrical Finish	3 days	Wed 11/16/11	Fri 11/18/11 41										
45	Punch List	3 days	Mon 11/21/11	Wed 11/23/11 44										
46	Clean up	2 days	Thu 11/24/11	Fri 11/25/11 45										
47	Inspection	1 day	Mon 11/28/11	Mon 11/28/11 46										
48	Completion	0 days	Mon 11/28/11	Mon 11/28/11 47										


Project: Five Palms Prelim 01Jun11 Date: Wed 6/1/11	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

FIVE PALMS PRELIMINARY SCHEDULE

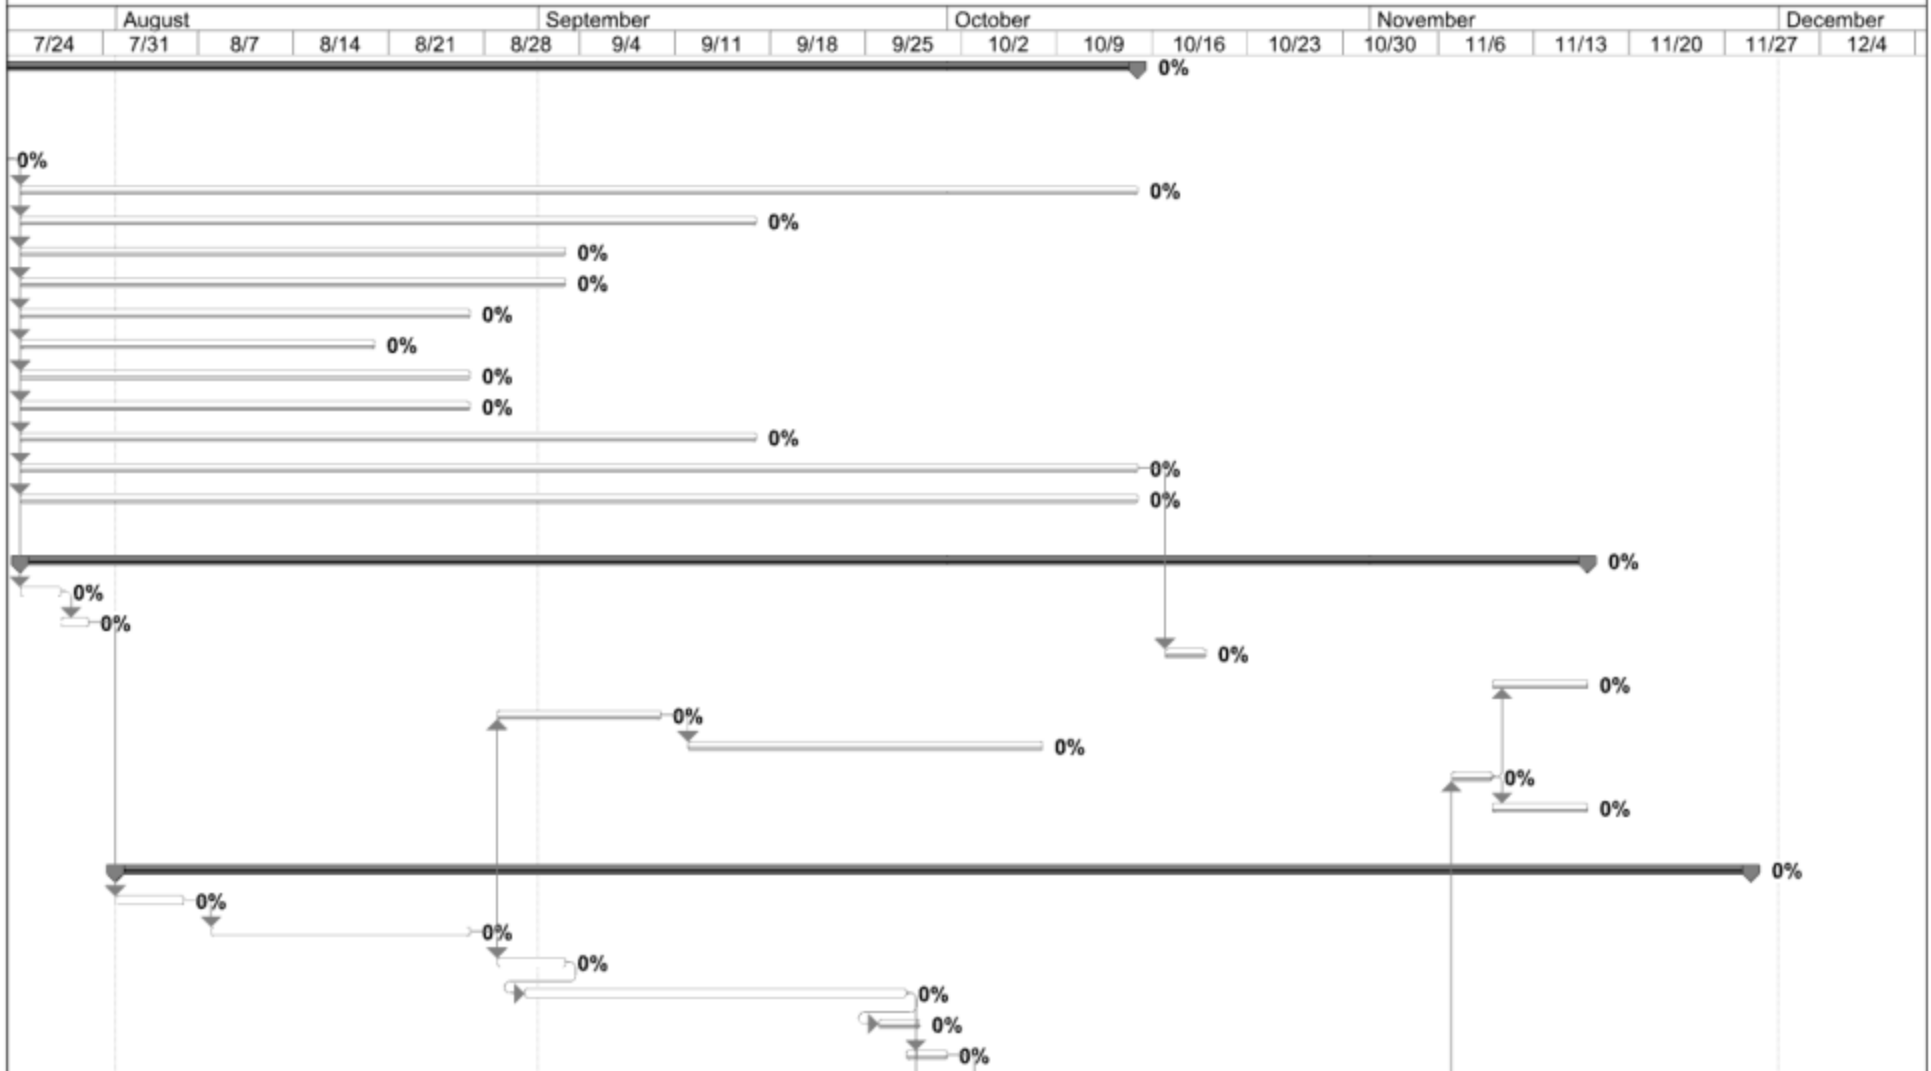

Project: Five Palms Prelim 01Jun11 Date: Wed 6/1/11	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

FIVE PALMS PRELIMINARY SCHEDULE

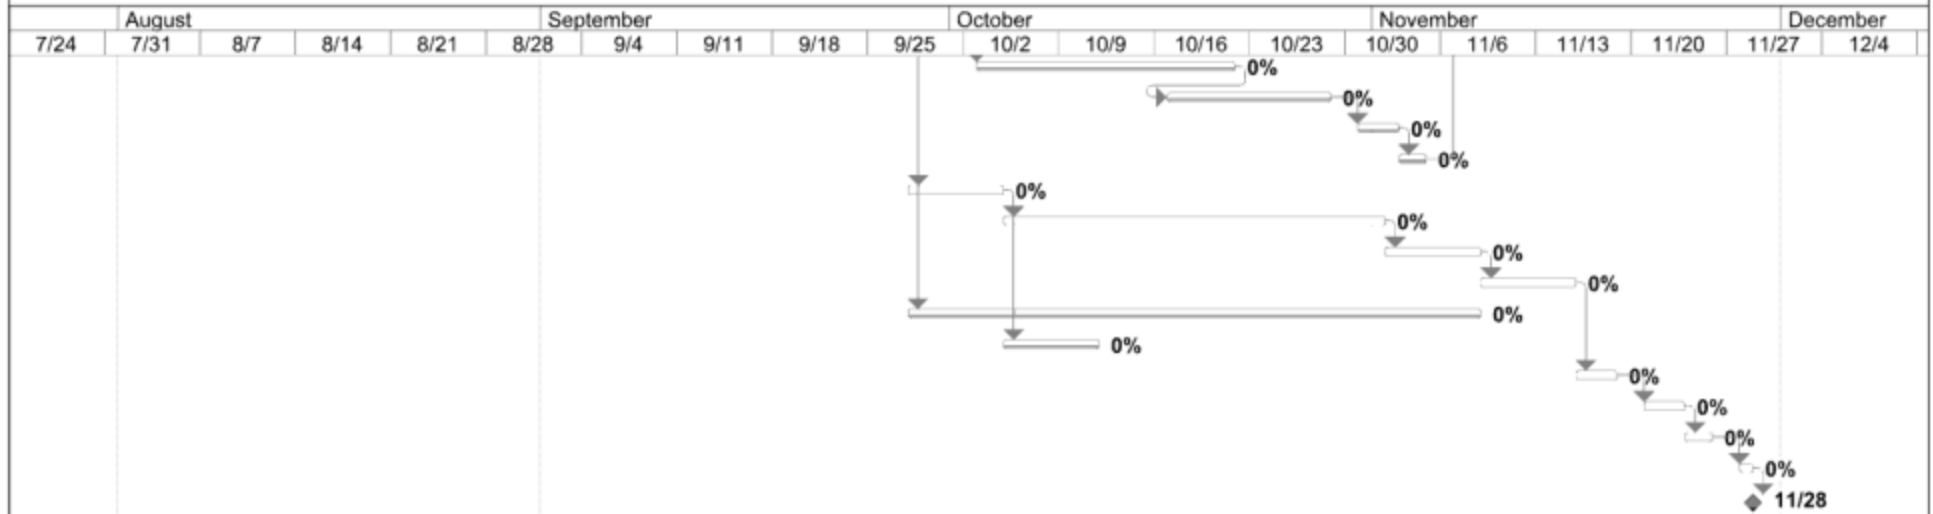

Project: Five Palms Prelim 01Jun11 Date: Wed 6/1/11	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			
